

ROADMAP REVIEW • END OF H1 2026

# Orbit H1 review

We committed to seven things, shipped five, and learned why the other two slipped.



# Against the H1 plan: five of seven shipped, two slipped for known reasons.

---

At the start of the year we committed to seven roadmap items. Five shipped on or ahead of plan. Two slipped — both for reasons we can name and both recoverable in H2. This review walks the plan versus what actually happened, and resets H2.



# What we committed to, and where each item landed.

| WORKSTREAM | Q1 PLAN       | Q2 PLAN            | STATUS          |
|------------|---------------|--------------------|-----------------|
| Search     | ✓ Relevance   | ✓ Typeahead        | ✓ On plan       |
| Billing    | ✓ Usage plans | – Invoicing v2     | – Slipped to Q3 |
| Mobile     | ✓ iOS parity  | ✓ Push             | ✓ On plan       |
| Reporting  | ✓ Dashboards  | ⌵ Scheduled export | ⌵ Cut from H1   |

✓ Shipped      – In flight      ⌵ Out of scope



# How delivery tracked against the plan we set in January.

5 / 7

Roadmap items shipped

TARGET 7 • TWO SLIPPED **AT RISK**



92%

Sprints hit commitment

TARGET 85% • AHEAD **ON PLAN**

+6 wk

Total schedule slip

CONCENTRATED IN BILLING **AT RISK**



IMPACT · SHIPPED FEATURES

# What the five shipped items did for customers.

*Measured 30 days after each launch, against the prior baseline.*

+22%

SEARCH SUCCESS RATE

+14%

MOBILE DAU

31%

OF REVENUE ON USAGE PLANS


4.7 / 5

FEATURE SATISFACTION



SLIPS • WHAT HAPPENED

# The story behind the two items that didn't land.

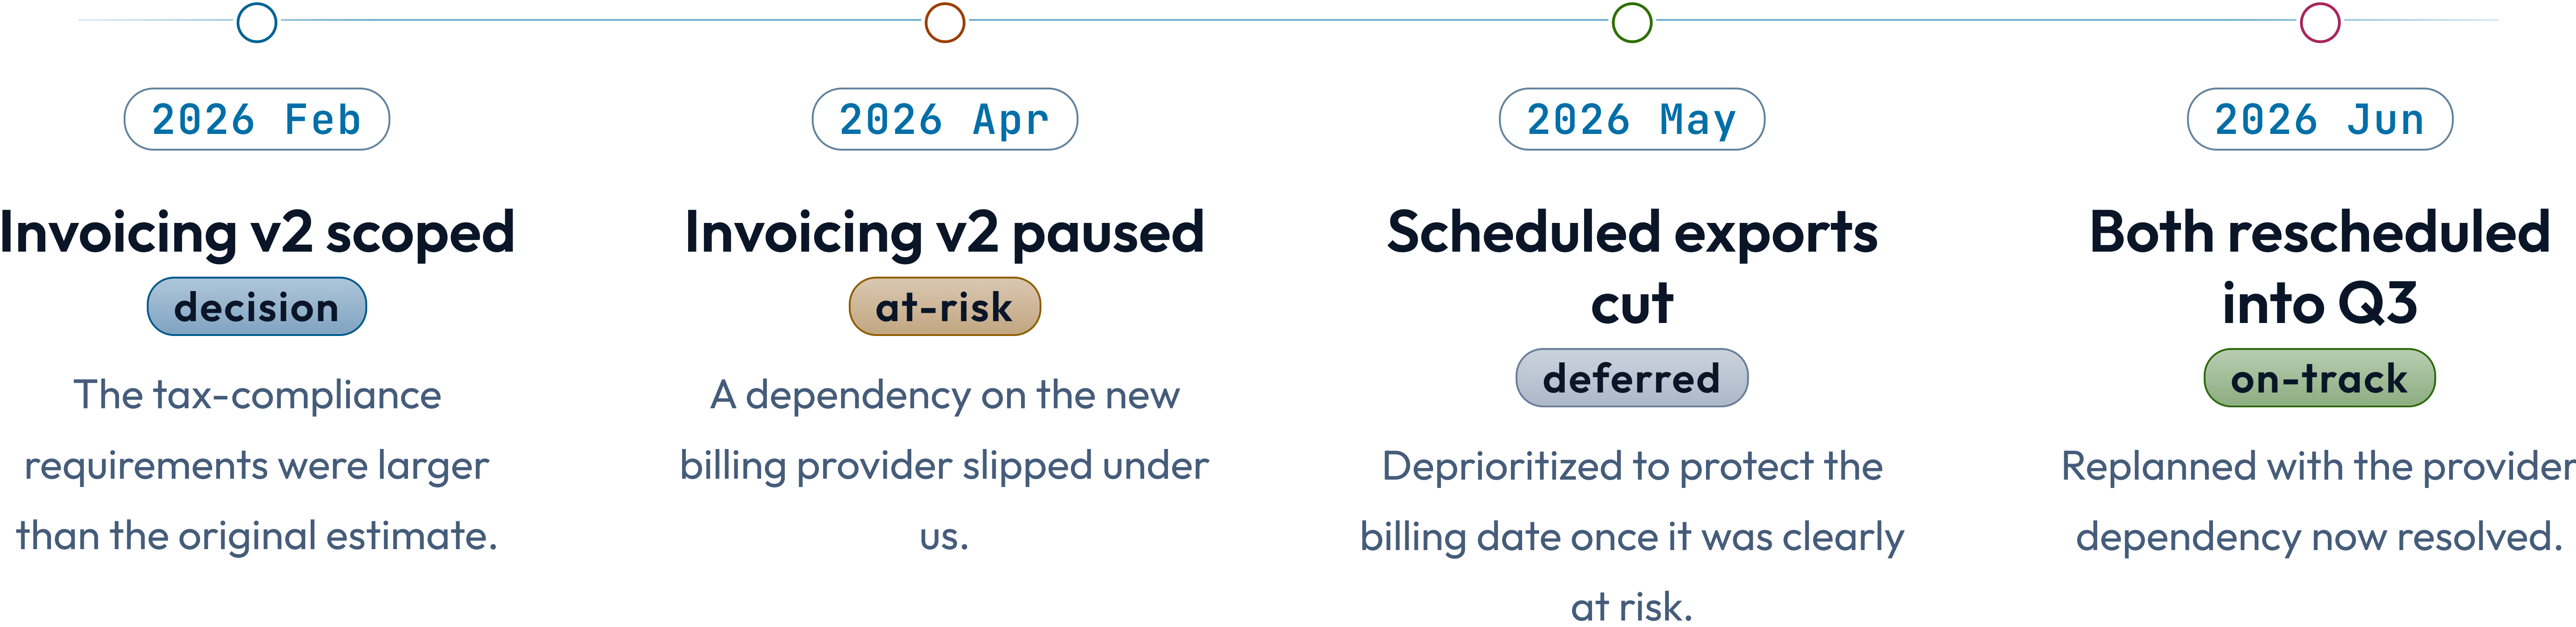



# What to keep doing and what to change, going into H2.

---

## **Worked • Keep.**

Tight sprint commitments held velocity steady

## **Worked • Keep.**

Shipping search and mobile in small increments

## **Struggled • Change.**

Estimating compliance-heavy work too lightly

## **Struggled • Fix first.**

Taking hard dependencies on unproven vendors



# The three changes we're carrying into H2 planning.

---

01

## **Spike compliance work first**

Any feature touching tax or legal gets a research spike before it's committed.

02

## **De-risk vendor dependencies**

No roadmap date depends on an unproven vendor without a fallback.

03

## **Commit to six, not seven**

Leave headroom so one slip doesn't cascade across the plan.



# The H2 plan, with the slipped work front-loaded.

| WORKSTREAM | Q3                  |  | Q4                   |  |
|------------|---------------------|--|----------------------|--|
|            | NOW                 |  | NEXT                 |  |
| Billing    | - Invoicing v2      |  | ○ Dunning automation |  |
| Reporting  | - Scheduled exports |  | ○ Report templates   |  |
| Search     | ○ Semantic search   |  | ○ Saved searches     |  |
| Mobile     | ○ Offline mode      |  | ○ Tablet layout      |  |

-

 In flight

○

 Planned



ORBIT PRODUCT · [PRODUCT@EXAMPLE.COM](mailto:PRODUCT@EXAMPLE.COM)

Five shipped, two replanned,  
three lessons carried forward.
