

KICKOFF • 12 JUNE 2026

# Project Northstar

Consolidating four sales tools into one CRM by year-end — here is the charter.

# We are consolidating four sales tools into one CRM by 19 December.

---

Sales runs on four disconnected tools today. Northstar replaces them with a single CRM so reps stop re-keying data and leadership gets one source of pipeline truth. This kickoff sets the charter: the why, the scope, the team, and the first decision.

# The problem: four tools, no single view, hours lost to re-entry.

---

Reps maintain the same account in a CRM, a quoting tool, a spreadsheet, and an email plugin. Nothing syncs. Forecasts are reconciled by hand every Friday, and no one trusts the number the same way twice.

- The sales team estimates six hours per rep per week lost to duplicate data entry.
- Three of the last four board forecasts were revised after the fact.

THE COST OF FRAGMENTATION

6 hrs

lost per rep, per week, to duplicate entry  
— across 90 reps, that is a full team  
doing nothing but re-typing.

# The charter: one CRM, one data model, live by 19 December.

---

Northstar delivers a single CRM with a unified account model, migrated history, and native quoting — replacing all four legacy tools. Success is measured by adoption and forecast trust, not by go-live alone.

- In scope: accounts, opportunities, quoting, and reporting.
- Out of scope: marketing automation and support ticketing — phase two.

# What "done" must satisfy before we decommission anything.

---

## 01 **Single source of truth**

Every account, opportunity, and quote lives in one system with no shadow spreadsheets.

---

## 02 **Clean migration**

All open opportunities and two years of closed history move with zero data loss.

---

## 03 **Reps actually use it**

90% weekly active adoption across the sales org within four weeks of launch.

---

## 04 **Forecast trust restored**

Leadership reads one pipeline number that reconciles without manual adjustment.

NORTHSTAR • H2 2026

# What ships in each phase, by workstream.

| WORKSTREAM | FOUNDATION                            | BUILD                                     | LAUNCH                                    |
|------------|---------------------------------------|-------------------------------------------|-------------------------------------------|
|            | JUL                                   | SEP                                       | DEC                                       |
| Data model | <div><div></div> Unified schema</div> | <div><div></div> History migration</div>  | <div><div></div> Cutover</div>            |
| Quoting    | <div><div></div> Requirements</div>   | <div><div></div> Native quote build</div> | <div><div></div> Pilot</div>              |
| Reporting  | <div><div></div> Forecast spec</div>  | <div><div></div> Dashboard build</div>    | <div><div></div> Leadership rollout</div> |
| Enablement | <div><div></div> Comms plan</div>     | <div><div></div> Training content</div>   | <div><div></div> Org-wide training</div>  |

In flight

Planned

# Who owns what on Northstar.

**Sponsors the project and clears blockers**

Dana Whitfield, VP Sales

Final escalation point; owns the go / no-go at each gate.

**Runs delivery day to day**

Marco Ruiz, Project Lead

Owns the plan, the standups, and the status you read each week.

**Owns the data model and migration**

Aisha Bello, Eng Lead

Accountable for schema, migration tooling, and zero-loss cutover.

**Owns adoption and training**

Tom Lindqvist, Enablement

Designs the rollout, the training, and the adoption metric.

# How we will work together for the next six months.

---

## **Weekly status**

A one-page written status every Friday, read before Monday's standup.

## **Decision log**

Every scope or design decision is logged with its rationale and owner.

## **Two-week sprints**


We plan and demo in two-week cycles; nothing waits a quarter for feedback.

## **Stage gates**

Three go / no-go gates — after Foundation, Build, and before Launch.

MILESTONES • H2 2026

# The dated path from kickoff to launch.

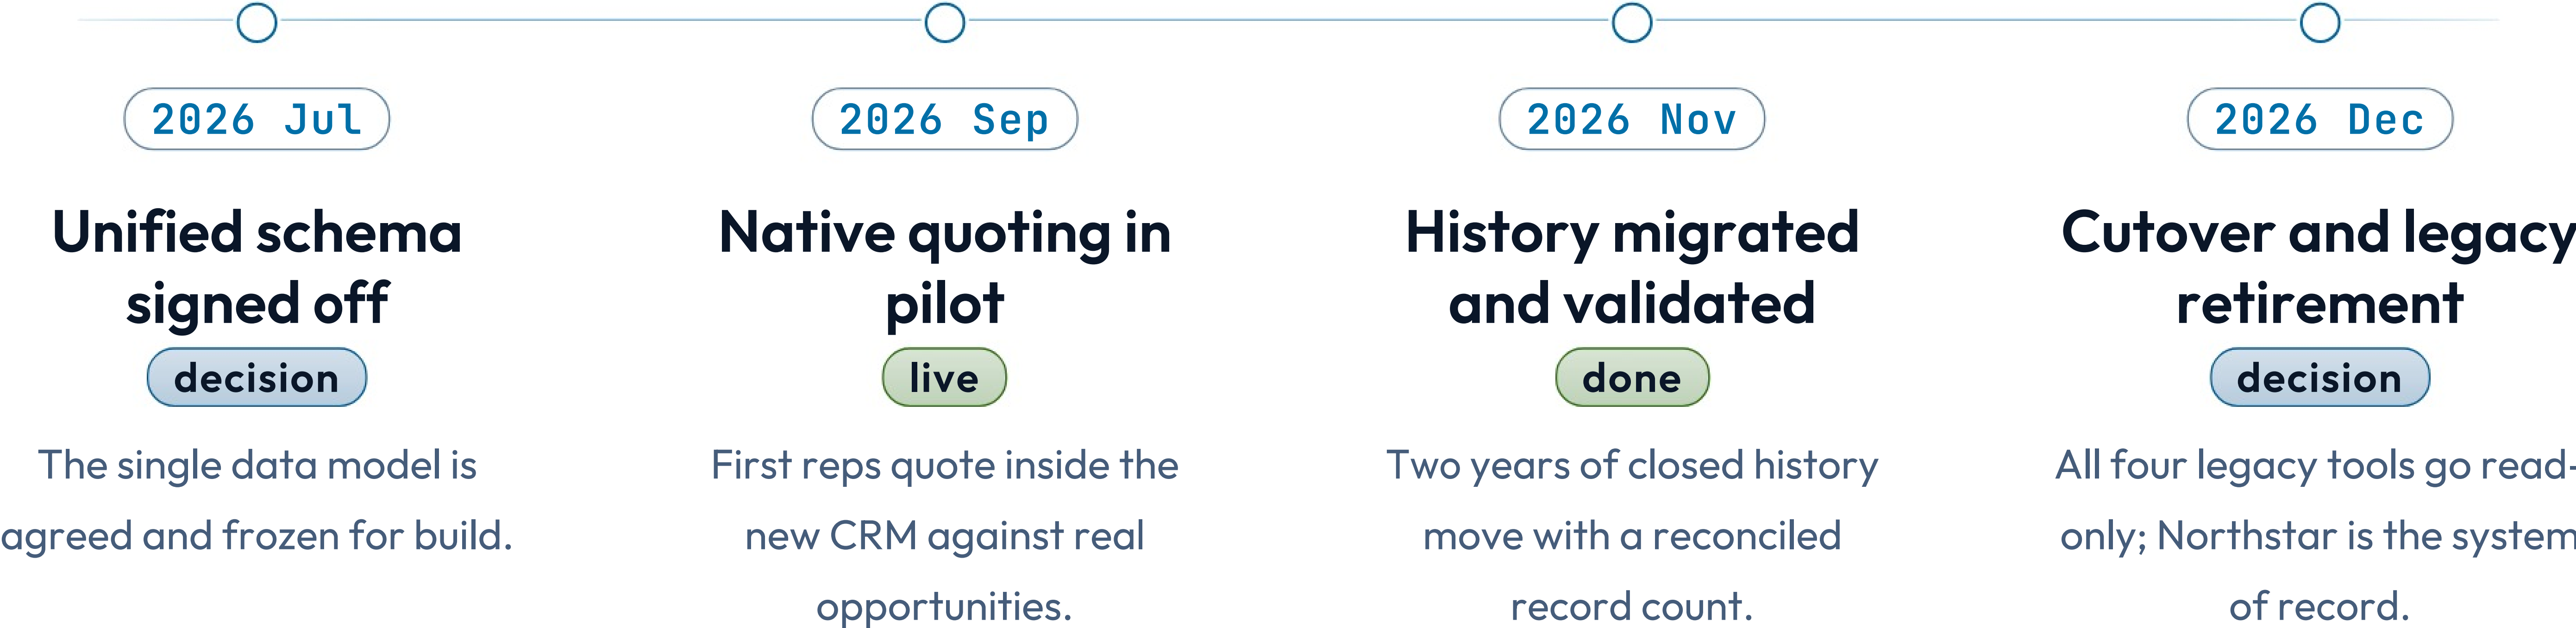

# First decision: freeze the data model before any build starts.

---

## **FREEZE THE SCHEMA FIRST**

Six weeks of design up front prevents months of rework downstream.

## **BUILD AND REFACTOR IN PARALLEL**

Feels faster early, but every schema change ripples through migration and quoting.

MARCO RUIZ • NORTHSTAR@EXAMPLE.COM

One CRM, one truth,  
live by year-end.
