

PLATFORM TEAM • WEEK OF 8 JUNE 2026

Lumen Platform

The checkout migration is on track for 1 July — one risk needs a decision today.

Bottom line: we ship checkout on Lumen 1 July, on plan, with one open call.

The migration of checkout to the Lumen platform is 78% complete and tracking to the 1 July cutover. Eleven of fourteen services are live in production. The only thing standing between us and the date is a load-testing decision I need from this room today.

Why this matters now: the legacy checkout stack goes end-of-support 31 July.

The vendor pulls security patches for the legacy stack at the end of July.

Migrating to Lumen before then keeps us supported and cuts our per-transaction cost by a third. Slipping past 1 July compresses the buffer between cutover and end-of-support to nothing.

- A clean two-week buffer is the difference between a calm launch and a forced one.
- Every week of delay is roughly \$40K in avoidable legacy hosting spend.

Eleven of fourteen live; latency and errors inside target.

78%

Services migrated

11 OF 14 • TARGET 100% BY 1 JUL ON PLAN

142 ms

p99 checkout latency

TARGET 180 MS ON PLAN

0.02%

Checkout error rate

TARGET 0.1% ON PLAN

SHADOW TRAFFIC • LAST 7 DAYS

What the shadow deployment is telling us before we cut over.

Lumen running in parallel with legacy, mirroring 100% of live checkout traffic.

4.1M

SHADOW TXNS
PROCESSED

99.98%

PARITY WITH
LEGACY

38


MISMATCHES
INVESTIGATED

0

UNRESOLVED
DISCREPANCIES

PROGRESS • Q2 2026

How the migration has unfolded since April.

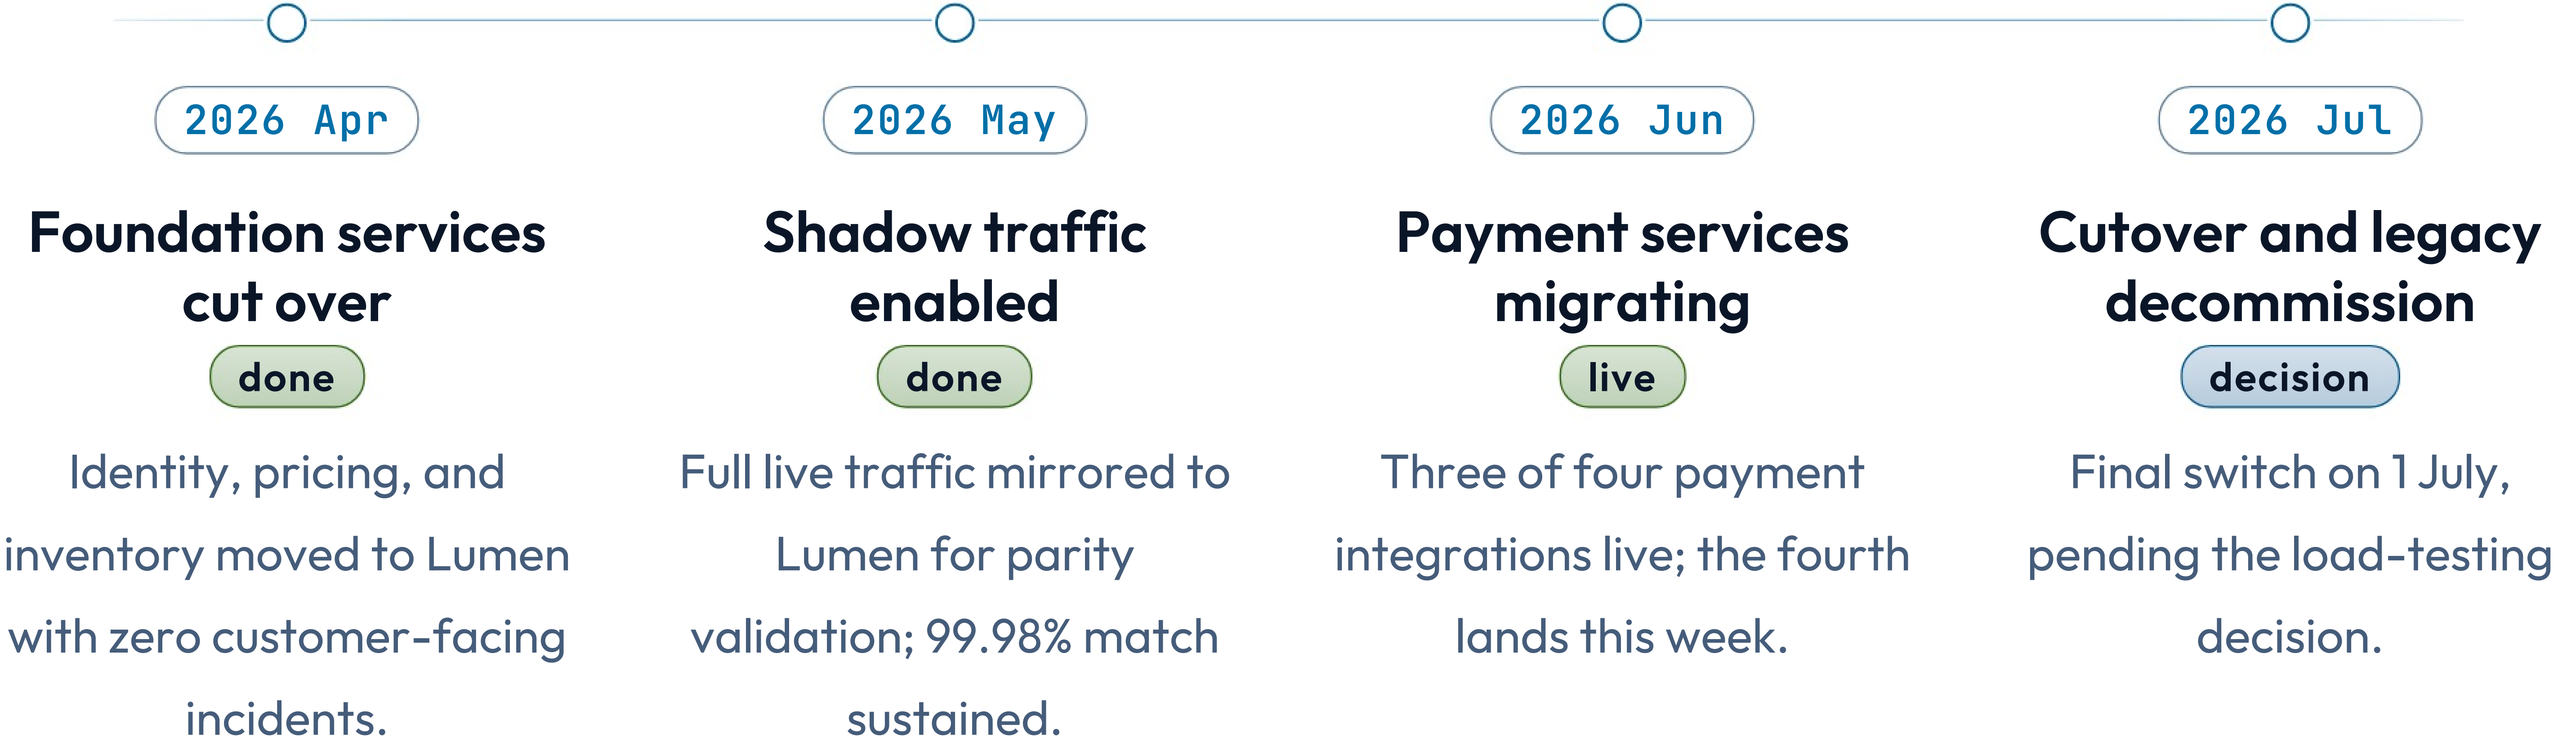

What remains, by workstream, before we flip the switch.

WORKSTREAM	THIS WEEK	NEXT WEEK	CUTOVER
	WK OF 8 JUN	WK OF 15 JUN	WK OF 29 JUN
Services	✓ Payments 3 of 4	– Final service	○ Decommission
Load testing	– Peak-load run	○ Sign-off	○ Standby
Runbook	✓ Draft complete	– Dry run	○ On-call brief

✓ Shipped – In flight ○ Planned

Where our open risks sit by likelihood and impact.

Low likelihood • Low impact.

Documentation lag on internal APIs

Low likelihood • High impact.

Payment-gateway timeout under peak load

High likelihood • Low impact.

Minor dashboard parity gaps post-cutover

High likelihood • High impact.

Unrehearsed peak load on cutover day

Cutover readiness as of today.

✓	Shadow parity sustained above 99.9%	7 days
✓	Runbook drafted and reviewed	Eng + SRE
—	Peak-load run	awaiting decision
—	Rollback procedure	dry-run pending
○	Final payment service live	this week
○	Executive go / no-go	25 Jun

Decision today: run a full peak-load rehearsal before cutover.

RUN THE PEAK-LOAD REHEARSAL

One day of effort buys certainty that checkout holds at Black-Friday volume.

CUT OVER ON SYNTHETIC TESTS ONLY

Saves a day but leaves the highest-impact risk unrehearsed on launch day.

PRIYA VENKAT • PLATFORM-TEAM@LUMEN.EXAMPLE

On track for 1 July — pending
your call on load testing.
