

ROADMAP REVIEW • END OF H1 2026

Orbit H1 review

We committed to seven things, shipped five, and learned why the other two slipped.

Against the H1 plan: five of seven shipped, two slipped for known reasons.

At the start of the year we committed to seven roadmap items. Five shipped on or ahead of plan. Two slipped — both for reasons we can name and both recoverable in H2. This review walks the plan versus what actually happened, and resets H2.

What we committed to, and where each item landed.

WORKSTREAM	Q1 PLAN	Q2 PLAN	STATUS
Search	✓ Relevance	✓ Typeahead	✓ On plan
Billing	✓ Usage plans	– Invoicing v2	– Slipped to Q3
Mobile	✓ iOS parity	✓ Push	✓ On plan
Reporting	✓ Dashboards	⌵ Scheduled export	⌵ Cut from H1

✓ Shipped – In flight ⌵ Out of scope

How delivery tracked against the plan we set in January.

5 / 7

Roadmap items shipped

TARGET 7 • TWO SLIPPED **AT RISK**



92%

Sprints hit commitment

TARGET 85% • AHEAD **ON PLAN**

+6 wk

Total schedule slip

CONCENTRATED IN BILLING **AT RISK**

IMPACT · SHIPPED FEATURES

What the five shipped items did for customers.

Measured 30 days after each launch, against the prior baseline.

+22%

SEARCH SUCCESS RATE

+14%

MOBILE DAU

31%


OF REVENUE ON USAGE PLANS

4.7 / 5

FEATURE SATISFACTION

SLIPS • WHAT HAPPENED

The story behind the two items that didn't land.

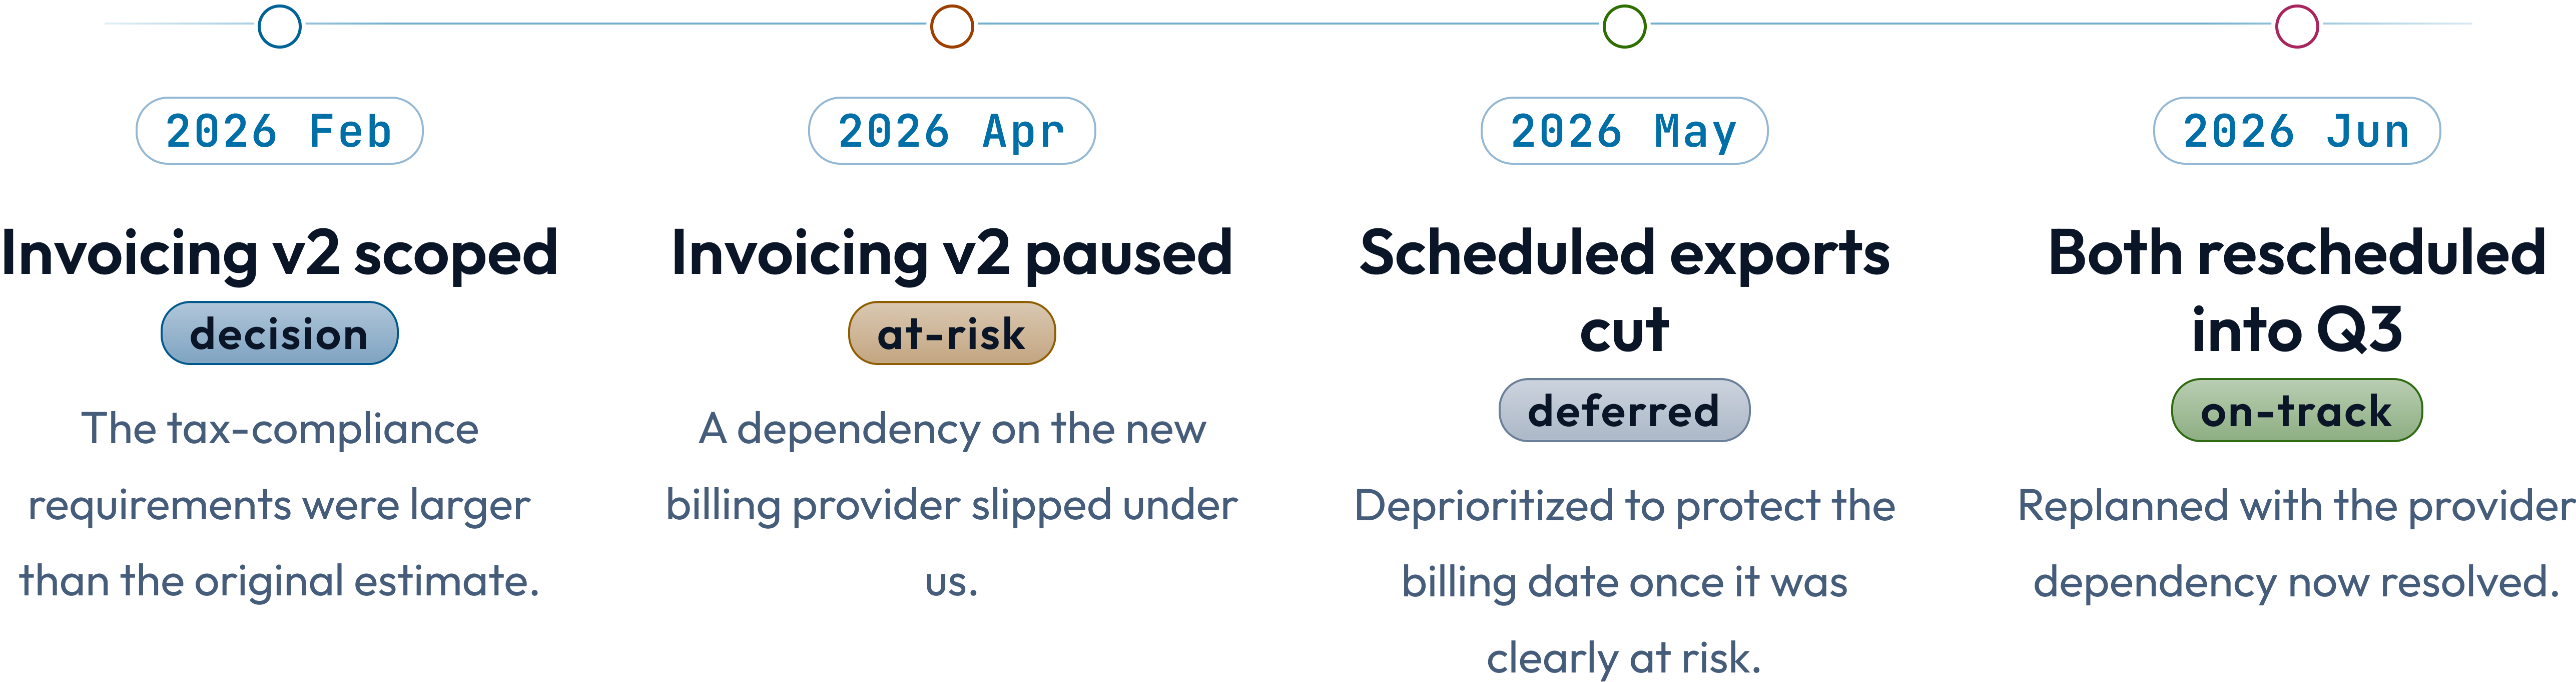

What to keep doing and what to change, going into H2.

Worked • Keep.

Tight sprint commitments held velocity steady

Worked • Keep.

Shipping search and mobile in small increments

Struggled • Change.

Estimating compliance-heavy work too lightly

Struggled • Fix first.

Taking hard dependencies on unproven vendors

The three changes we're carrying into H2 planning.

01

Spike compliance work first

Any feature touching tax or legal gets a research spike before it's committed.

02

De-risk vendor dependencies

No roadmap date depends on an unproven vendor without a fallback.

03

Commit to six, not seven

Leave headroom so one slip doesn't cascade across the plan.

The H2 plan, with the slipped work front-loaded.

WORKSTREAM	Q3	Q4
	NOW	NEXT
Billing	Invoicing v2	Dunning automation
Reporting	Scheduled exports	Report templates
Search	Semantic search	Saved searches
Mobile	Offline mode	Tablet layout

In flight Planned

ORBIT PRODUCT · PRODUCT@EXAMPLE.COM

Five shipped, two
replanned, three
lessons carried
forward.
