

RFP DPR-2027-04 • ORAL PRESENTATION

Permitting System Replacement

Our proposal to replace the county's 22-year-old building-permit system within 18 months.

We understand the goal: cut permit turnaround from weeks to days, without a risky big-bang cutover.

The county's permitting backlog is a constituent-service problem before it is a technology one. Our approach modernises in phases, keeps the legacy system live until each module is proven, and ships a measurable turnaround improvement in the first six months.

We have read the problem behind the requirements.

The RFP asks for a new system. The real requirement is faster, more predictable permits for residents and contractors, delivered without the failed cutover that derailed the 2021 attempt. Our proposal is shaped to that outcome, not just the feature list.

How our approach meets each evaluation criterion.

- 01 Phased, low-risk delivery**
Module-by-module rollout with the legacy system live as fallback until each phase is proven.

- 02 Demonstrated turnaround gain**
A measurable reduction in permit cycle time inside the first two phases, not at the end.


- 03 Open, portable architecture**
Standards-based and exportable; no proprietary lock-in to us as a vendor.

- 04 Accessibility & multilingual**
WCAG 2.1 AA and three-language intake from first release.

Our approach: ship value in phases, never a big-bang cutover.

We deliver the highest-volume permit types first, run them in parallel with the legacy system, and migrate the rest only once each module is proven in production. The 2021 attempt failed on a single cutover; ours cannot fail that way.

The 18-month delivery plan, by workstream.

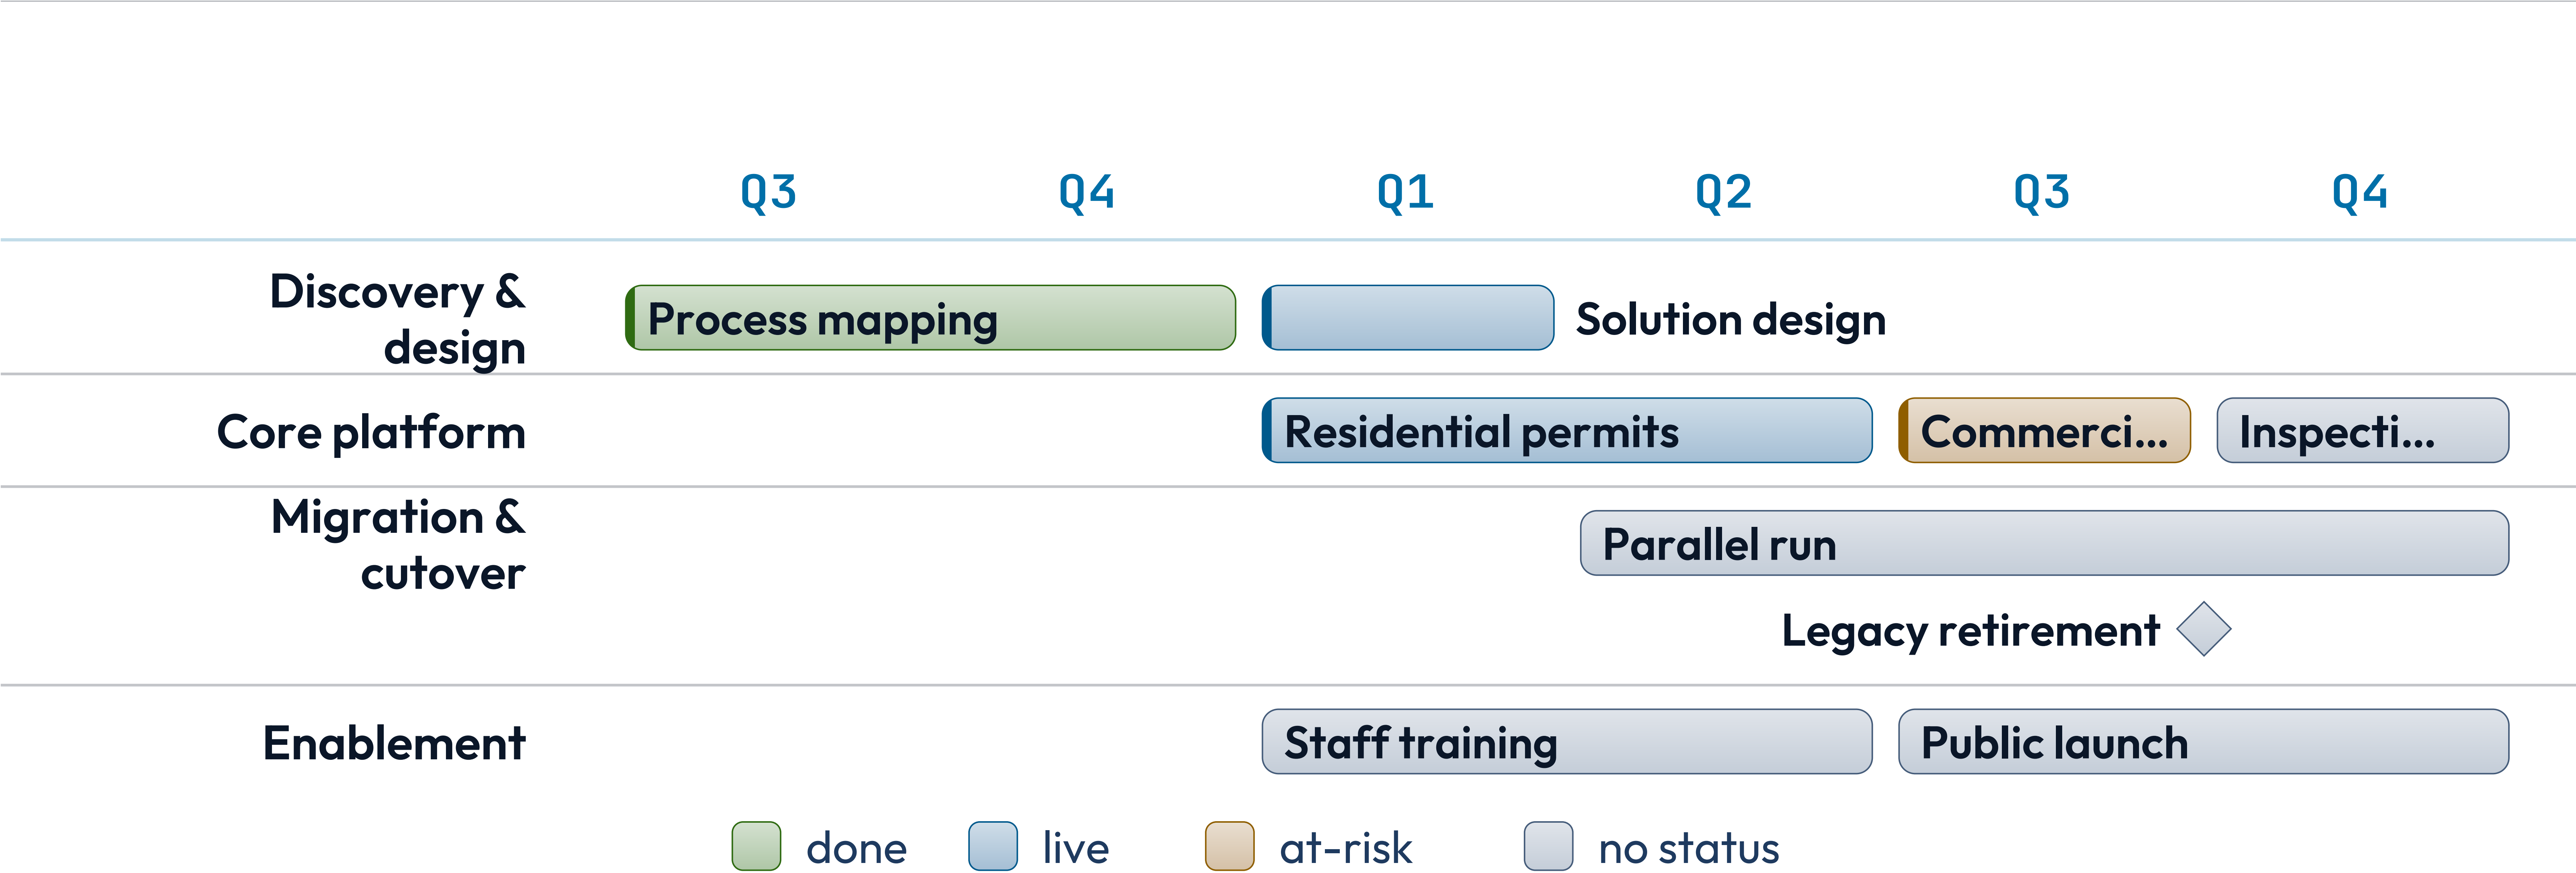

The team accountable for delivery.

Engagement lead

Dana Whitfield

14 years in public-sector permitting; led three county system replacements to completion.

Solution architect

Raj Patel

Designed the standards-based core; owns the portability and integration commitments.

Delivery manager

Lena Osei

Runs the phased rollout and the parallel-run discipline; single point of accountability.

Change & training lead

Marco Reyes

Owns staff enablement and the public-launch communications plan.

Our relevant record on comparable engagements.

- | | | |
|----|----------------------------|---|
| 01 | Coastal County permits | 19-month phased replacement. Turnaround cut from 26 days to 6. On budget. |
| 02 | Metro inspections platform | Inspections and scheduling module; 40% fewer re-inspections. Delivered early. |
| 03 | State licensing portal | Multilingual, WCAG-AA intake serving 2.1M residents. Zero accessibility findings. |
| 04 | Regional GIS integration | Parcel and zoning data integration reused as the base for this proposal. |

Why the phased approach is the risk story, not a slower one.

A big-bang cutover concentrates all risk on one date — the failure mode of the 2021 attempt. Phasing spreads risk across modules, each independently reversible. The county sees benefit in month six and never bets the whole service on a single go-live.

VALUE • COMMITTED OUTCOMES

What we commit to deliver, with the numbers we will be held to.

6 days

Median permit turnaround

DOWN FROM 24 DAYS **ON PLAN** SLA

18 mo

To full replacement

PHASED, FIXED-PRICE **ON PLAN**
DELIVERY

\$0

Cost of a failed cutover

PARALLEL-RUN GUARANTEE **ON PLAN**
RISK

VALUE • YEAR-ONE IMPACT

The return the county sees inside the first twelve months.

–58%

Permit cycle time

RESIDENTIAL PERMITS, PHASE ONE ON PLAN OUTCOME

92%

Applications filed online

UP FROM 31% ON LEGACY ON PLAN OUTCOME

–36%

Counter & call volume

STAFF REDEPLOYED TO REVIEW ON PLAN OUTCOME

MERIDIAN CIVIC PARTNERS • PROPOSALS@MERIDIANCIVIC.EXAMPLE

A faster permit in six months,
a finished system in eighteen
— without the cutover risk.
